

Notice of Public Meeting
Tuesday, March 10, 2026
10:00 a.m.

**JUDICIARY & PUBLIC
SAFETY COMMITTEE**

Door County Government Center
County Board Room – 1st Floor
421 Nebraska Street, Sturgeon Bay

Oversight for Clerk of Courts, Circuit Court, Family Court/Register in Probate, District Attorney, Emergency Services Department, Emergency Management, Communications Department, and Sheriff's Office

AGENDA

1. Call Meeting to Order
2. Establish a Quorum
3. Adopt Agenda / Properly Noticed
4. Approve Minutes of February 10, 2026 Regular Judiciary and Public Safety Committee Meeting
5. Correspondence
6. Public Comment
7. Supervisor Response
8. New Business (Review/Action)
 - **Towers/Communications Plan**
 - Fish Creek Tower Update
 - New 800MHz System Update
 - **Sheriff's Office**
 - FYI: Wisconsin County Mutual ALERT Grant Award
 - Review/Approve: SGTS. Three Year Contract Extension
 - **Emergency Services & Emergency Management**
 - FYI – Monthly Report
 - Outsourcing of Billing Services – Update
 - Review/Approve: 2025 Carryforward
 - Review/Approve: ES Write-Offs
 - Addressing Project – Update
 - Resolution 2026-__ - Acceptance of Door County Community Foundation Grant – Safety Barriers
 - **Communications**
 - FYI – Monthly Report
 - Review/Approve: 2025 Carryforwards
9. Sustainability Matters to be Considered
10. Legislative Matters to be Considered
11. Request for Agenda Items for Next Month's Meeting
12. Next Meeting Date: TBD
13. Adjourn

This meeting will be conducted by teleconference or video conference. Members of the public may join the meeting remotely or in-person

Please click the link below to join the webinar:

When: Mar 10, 2026 10:00 AM Central Time (US and Canada)
Topic: Judiciary & Public Safety Committee Meeting

Join from PC, Mac, iPad, or Android:

<https://us02web.zoom.us/j/82339237399?pwd=ilGhqMccpl8nbFebB5KgPOwuwMCdDI.1>

Webinar ID: 823 3923 7399
Passcode: 137304

To Connect via phone:
1-312-626-6799

Deviation from the order shown may occur

MINUTES
Tuesday, February 10, 2026

**JUDICIARY & PUBLIC
SAFETY COMMITTEE**

Door County Justice Center
Multipurpose Room – Room C185
1201 S. Duluth Ave., Sturgeon Bay

Oversight for Clerk of Courts, Circuit Court, Family Court/Register in Probate, District Attorney, Emergency Services Department, Emergency Management, Communications Department, and Sheriff's Office

Call Meeting to Order

The Tuesday, February 10, 2026 Judiciary & Public Safety Committee meeting was called to order by Chairman Joel Gunnlaugsson at the Door County Government Center at 10:03 a.m.

"These minutes have not been reviewed by the oversight committee and are subject to approval at the next regular committee meeting."

Establish a Quorum

Committee Members Present: Joel Gunnlaugsson, Ryan Shaw, Philip Rockwell (online), Collin Jeanquart, Nancy Robillard and Dale Vogel.

Others Present: Administrator Ken Pabich, Corporation Counsel Sean Donohue, Chief Deputy Kyle Veesser, ES Director Aaron LeClair, EM Director Jeb Saelens, Communications Director Brenda Bley, Finance Director Steve Wipperfurth, and Public.

Adopt Agenda / Properly Noticed

Motion by Robillard, seconded by Shaw to adopt the agenda. Motion carried by voice vote.

Approve Minutes of December 9, 2025 Regular Judiciary and Public Safety Committee Meeting

Motion by Shaw, seconded by Jeanquart to approve the minutes of the December 9, 2025 Judiciary & Public Safety Committee meeting. Motion carried by voice vote.

Correspondence

None.

Public Comment

None.

Supervisor Response

None.

New Business (Review/Action)

Towers/Communications Plan

No new business

Sheriff's Office

No new business

Emergency Services & Emergency Management

FYI – Monthly Report

ES Director Aaron LeClair reviewed the December 2025 and January 2026 report included in the meeting packet.

EM Director Saelens provided an update on disaster funding for the August 9th storm. The State applied for federal funding but it was denied. Saelens states they did appeal the decision but that was also denied. The county applied for \$93,689.21 in federal funding but will not be able to recoup the funds due to the denial. The municipalities will be able to apply for funds through the Wisconsin Disaster Fund through the state level.

Saelens states the county did receive the EMPG and EPCRA funding for 2025 with the same values as in the past.

Saelens updates the committee on the employee action plan, Rescue Task Force training is being held at the Government Center and is going well. Working on how to communicate within the Government Center on situational awareness plan.

Saelens states he is hosting PIO training March 13-15, 2026 and ICS training for Public Officials February 21, 2026.

Update on Addressing Project

Saelens reported the addressing project is 26.14% complete and going well; had a setback with the cold weather.

Outsourcing of Billing Services – Update

EMS Director LeClair explains they went live on February 1, 2026, will have feedback in the coming weeks.

Proposed Middle EMS Station – Staff Recommendation

EMS Director LeClair reviews Call Data Overlay slides (attached). The slides depict three proposed sites: CTH T & CTH V; Egg Harbor Village Fire Station and Jacksonport Fire Station with response times. LeClair recommends building a stand-alone station in the area of CTH T and CTH V as that site would best help reduce response times for ambulances in the middle section of the peninsula. Motion by Jeanquart, seconded by Shaw to send on to County Board to evaluate the possible location and land acquisition in the area of CTH V and CTH T. Motion carried by unanimous voice vote.

Communications

FYI – Monthly Report

Communications Director Brenda Bley reviewed the monthly reports for December 2025 and January 2026 included in the meeting packet. Bley reported staffing currently has two vacancies. The backup dispatch centers have been installed at BUG Fire, one is up and running and will be used for training in the near future.

Sustainability Matters to be Considered

No matters were presented.

Legislative Matters to be Considered

No matters were presented.

Request for Agenda Items for Next Month's Meeting

Nothing as of this meeting.

Next Meeting Date

Tuesday, March 10, 2026 – 10:00 a.m.


Adjourn

Motion by Shaw, seconded by Jeanquart to adjourn. Motion carried by voice vote. Time: 10:43 a.m.

Respectfully submitted by Diane Franklin, Administrative Assistant

Emergency Services Buildings Existing locations January 13th, 2026


Map #9 - County hwy T & V
2023 Call Data Overlay
Proposed Site Drive Times

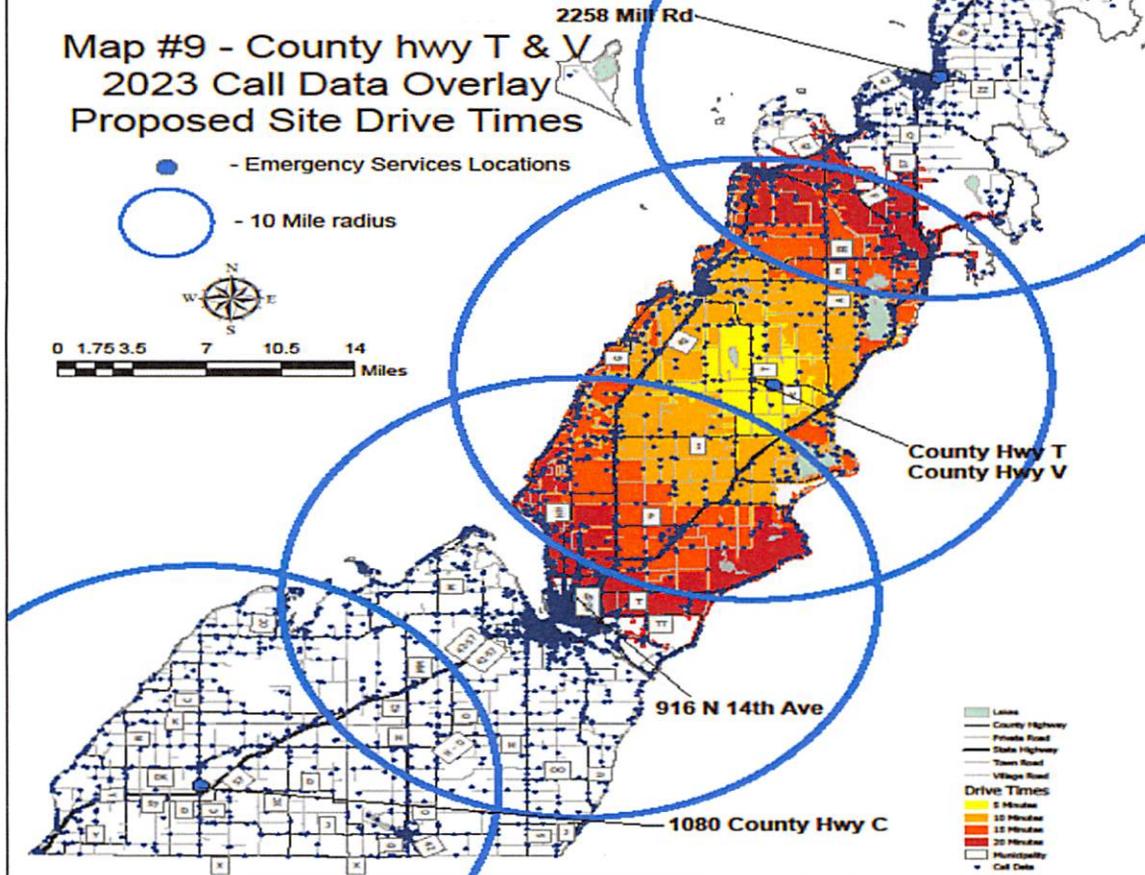

2023 Call Data Overlay Proposed Site Drive Times


● - Emergency Services Locations

○ - 10 Mile radius

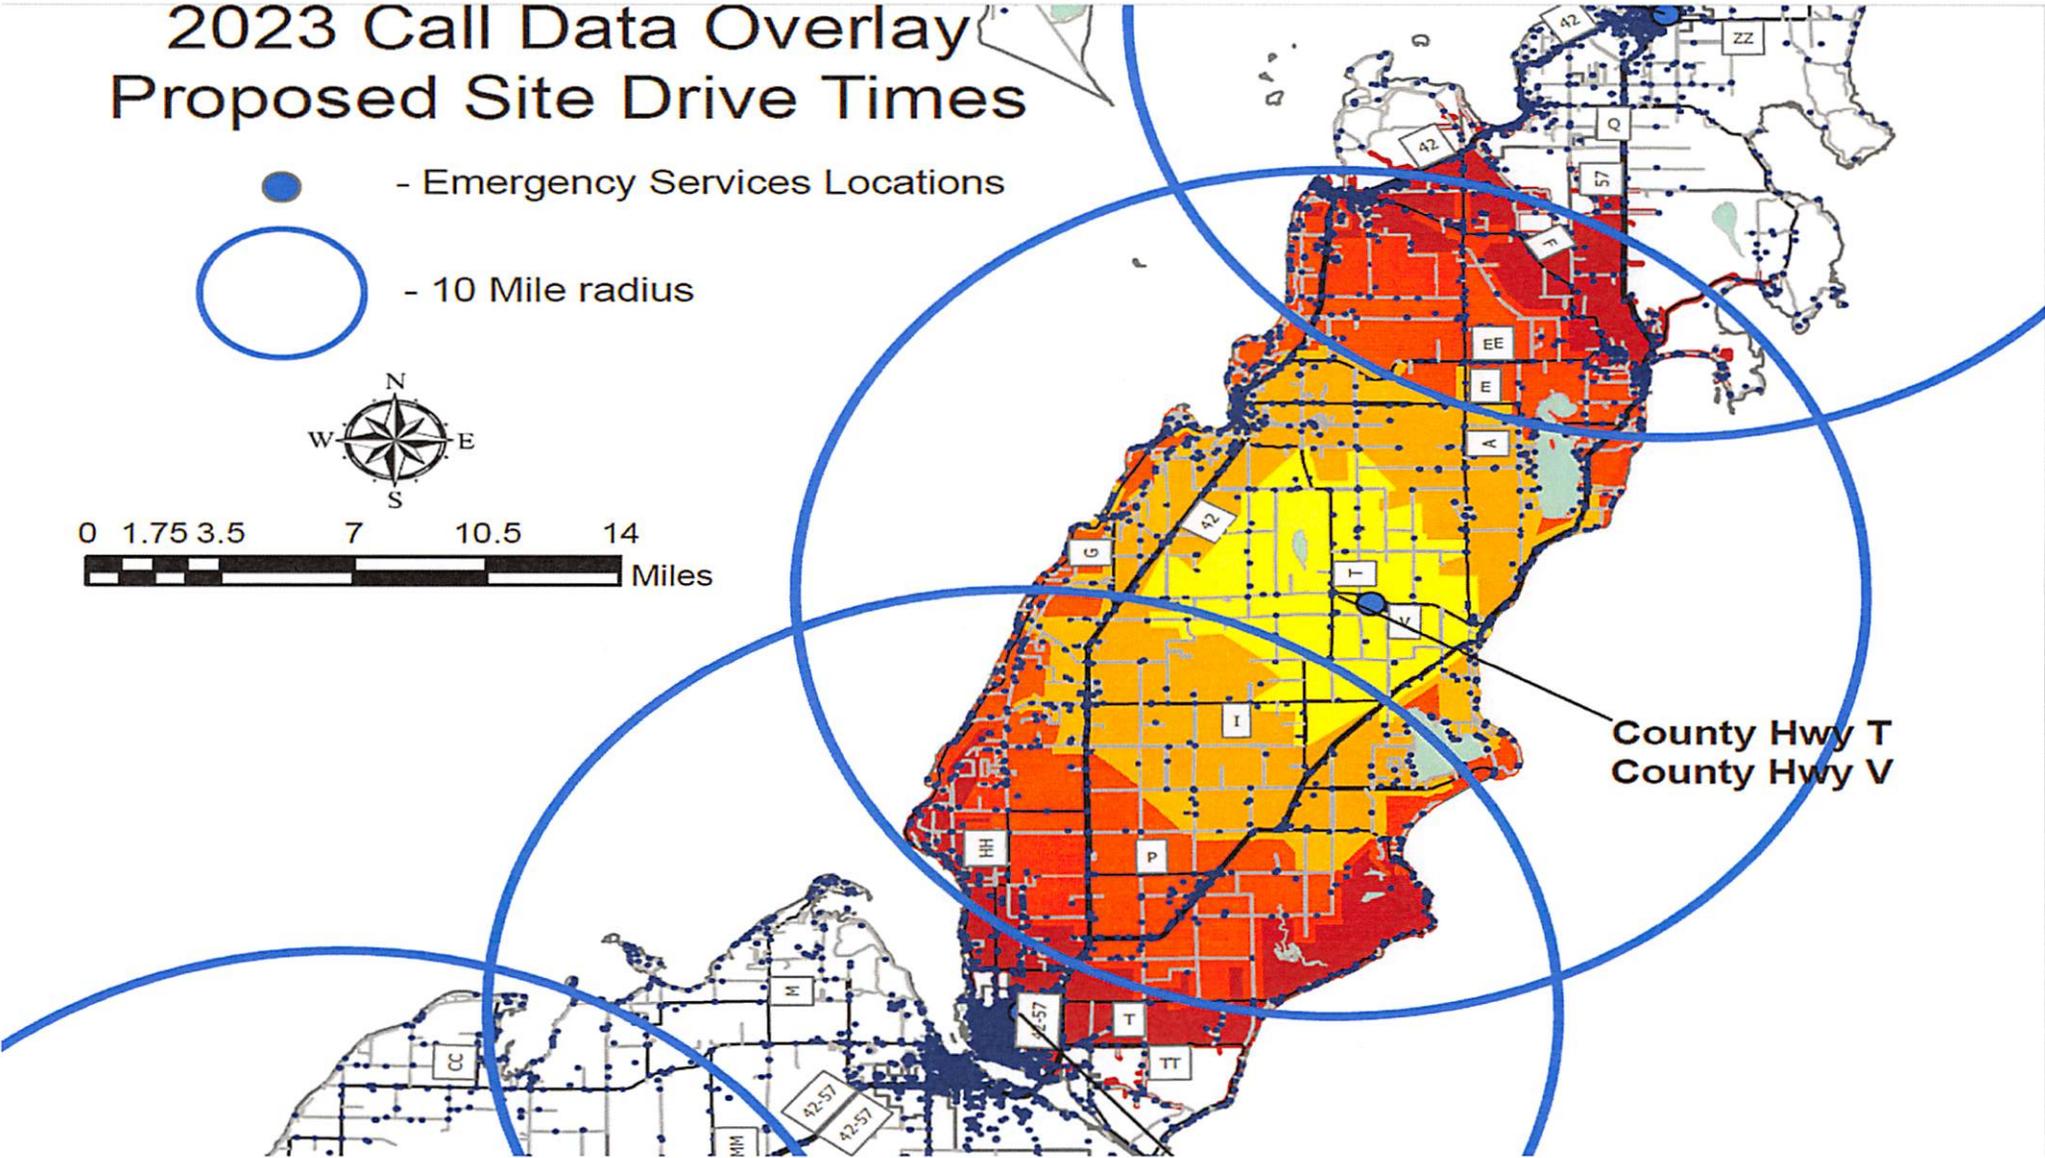

Emergency Services Buildings Existing locations January 13th, 2026

Map #8 - Village Fire Station
2023 Call Data Overlay
Proposed Site Drive Times

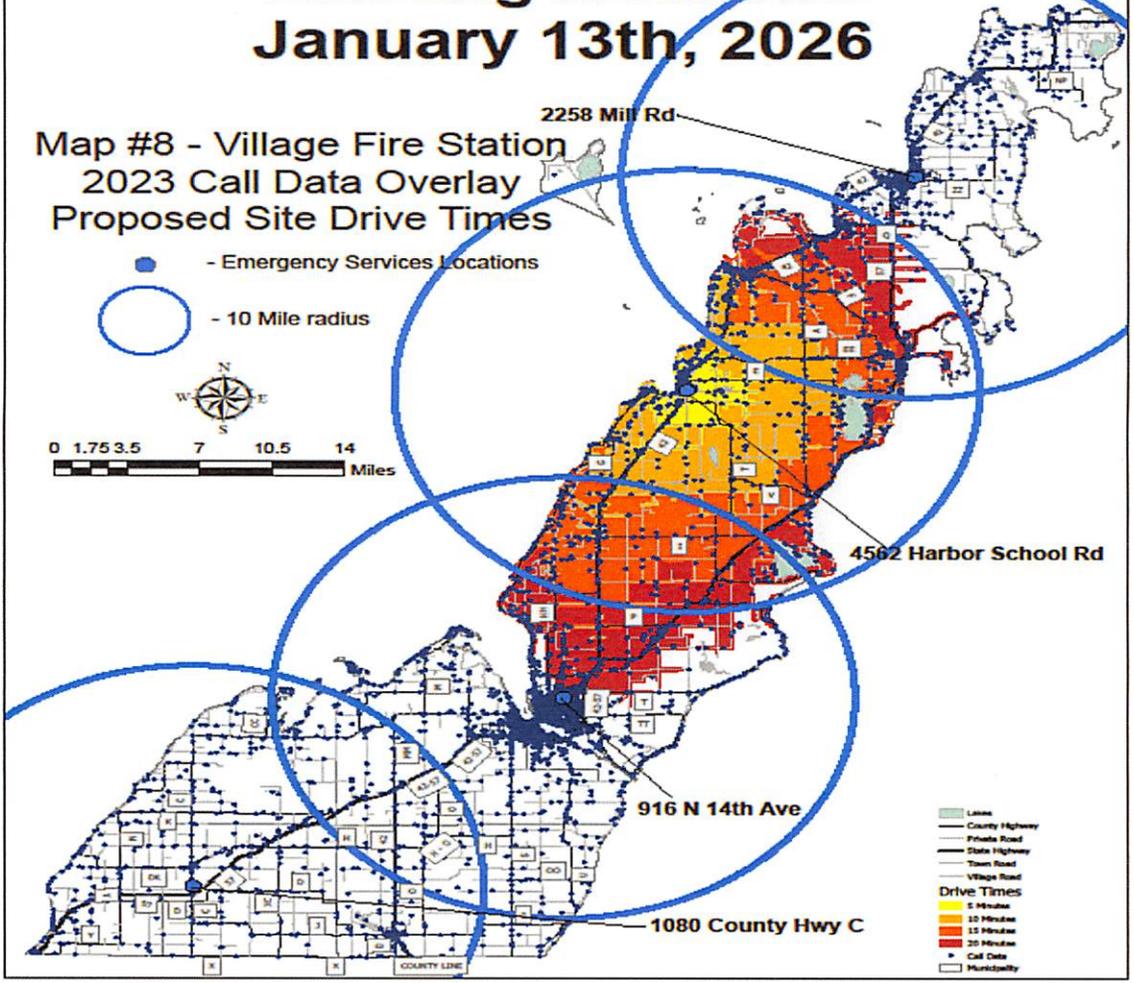


Map #8 - Village Fire Station 2023 Call Data Overlay Proposed Site Drive Times

● - Emergency Services Locations

○ - 10 Mile radius




0 1.75 3.5 7 10.5 14 Miles

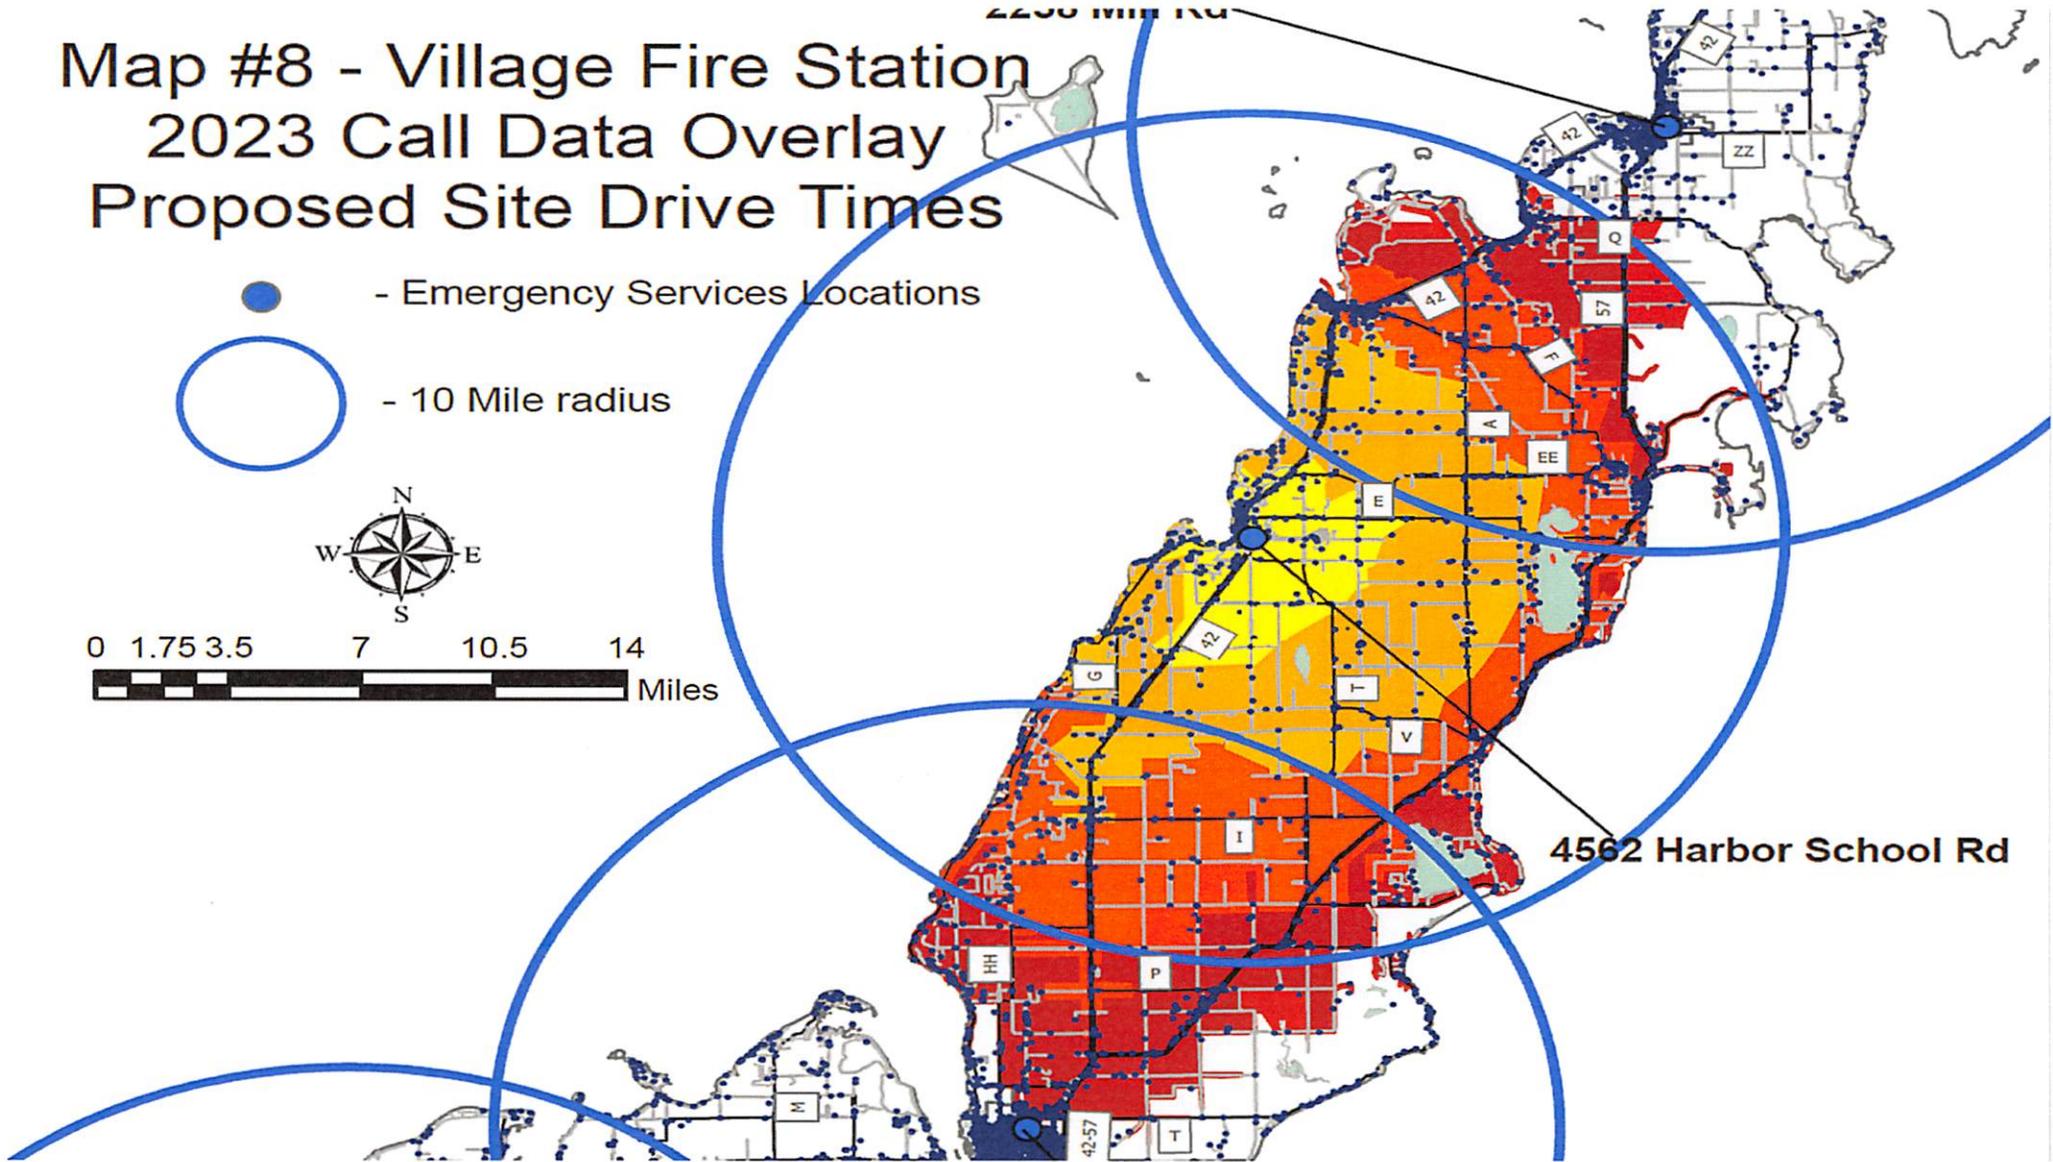

Emergency Services Buildings Existing locations January 13th, 2026

Map #7 - Jacksonport Fire
2023 Call Data Overlay
Proposed Site Drive Times

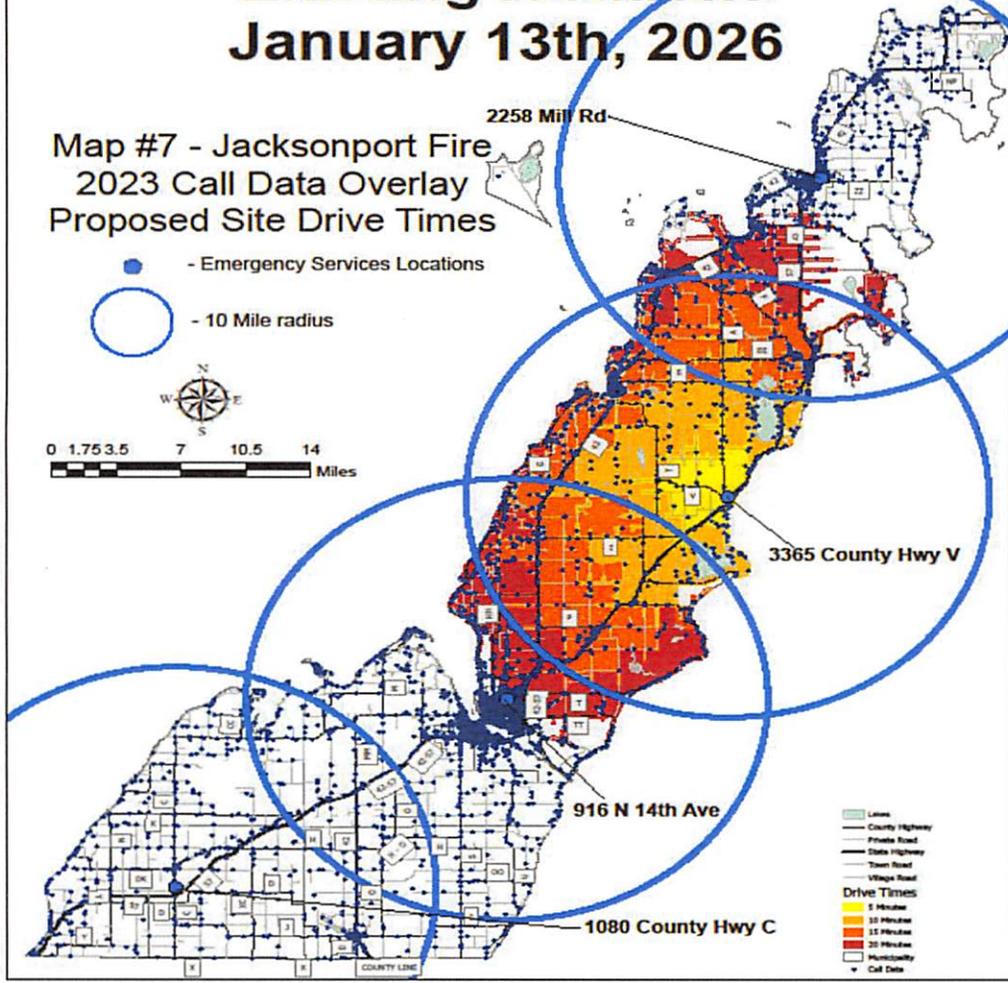


Map #7 - Jacksonville Fire 2023 Call Data Overlay Proposed Site Drive Times

● - Emergency Services Locations

○ - 10 Mile radius



0 1.75 3.5 7 10.5 14 Miles


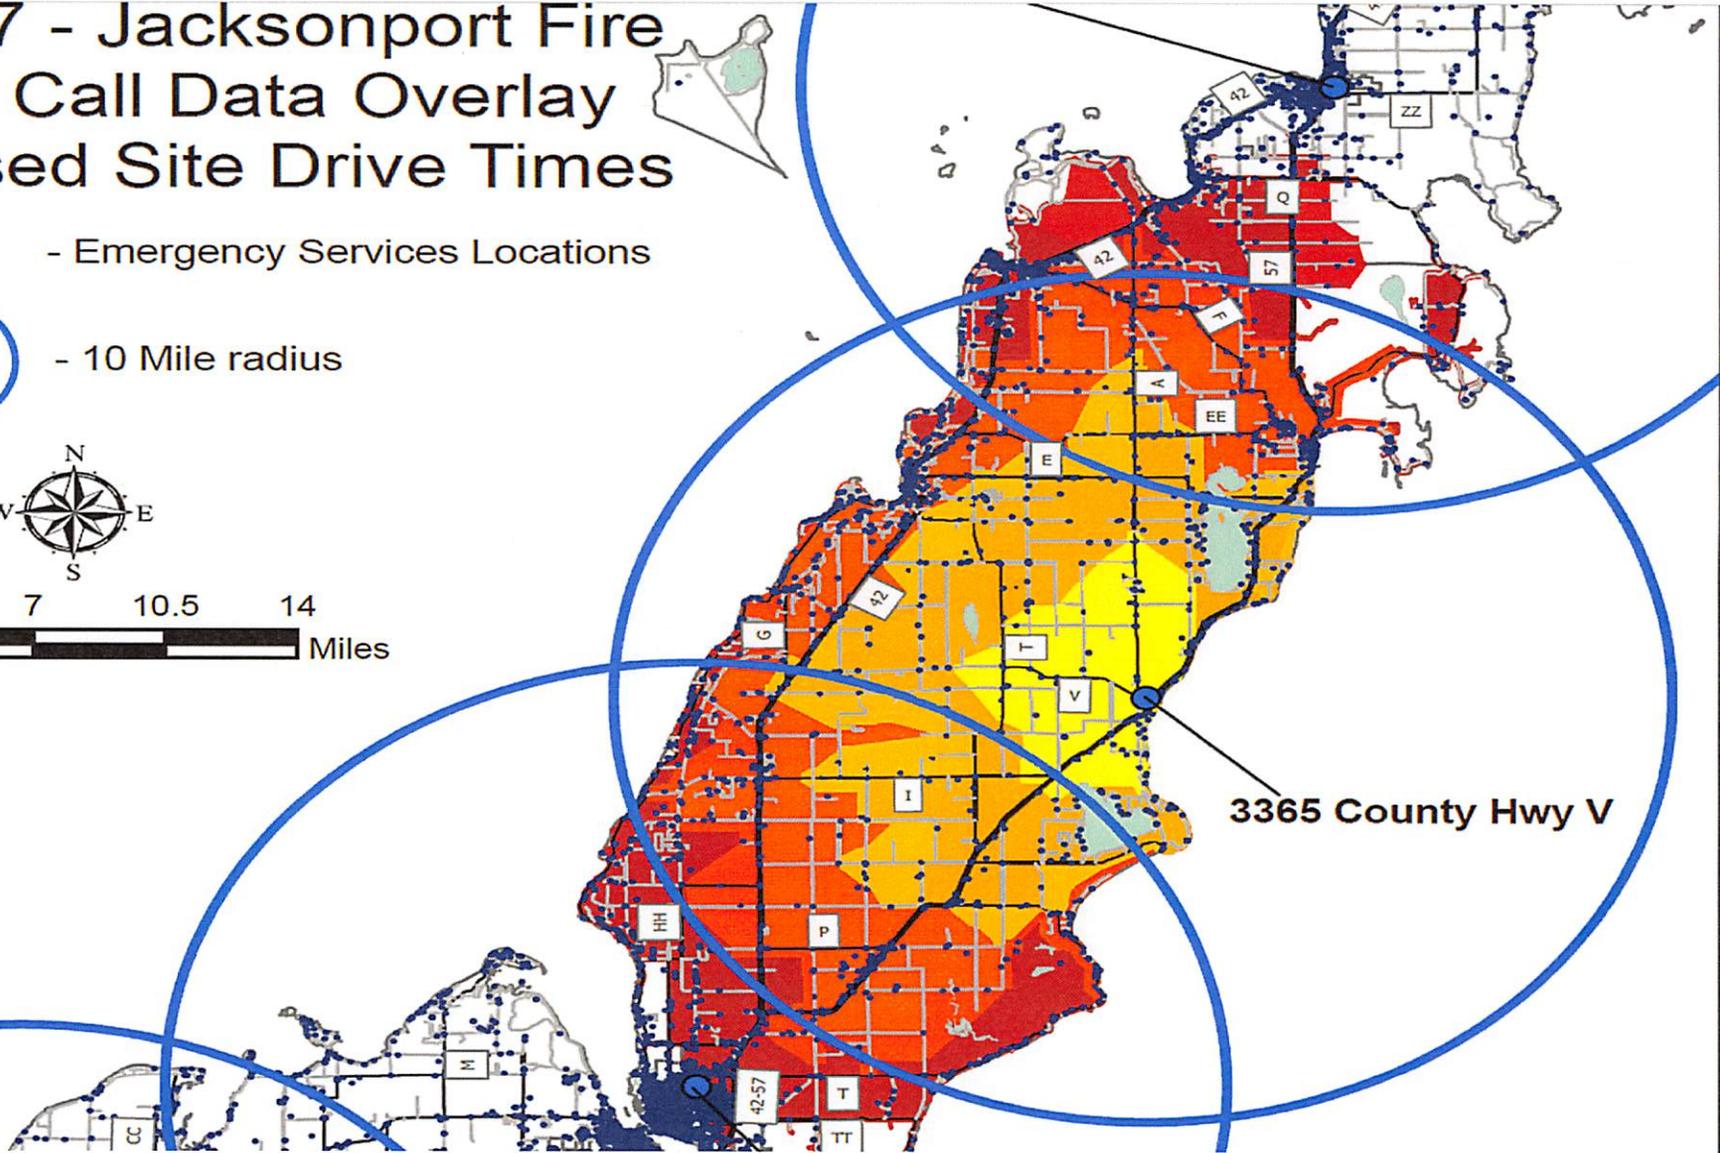


3365 County Hwy V


Emergency Services Buildings Existing locations

Map #16 (additional)
County Hwy T & V
15 Minutes Drive Time
Existing Site Drive Times


- - Emergency Services Locations
- - 10 Mile radius

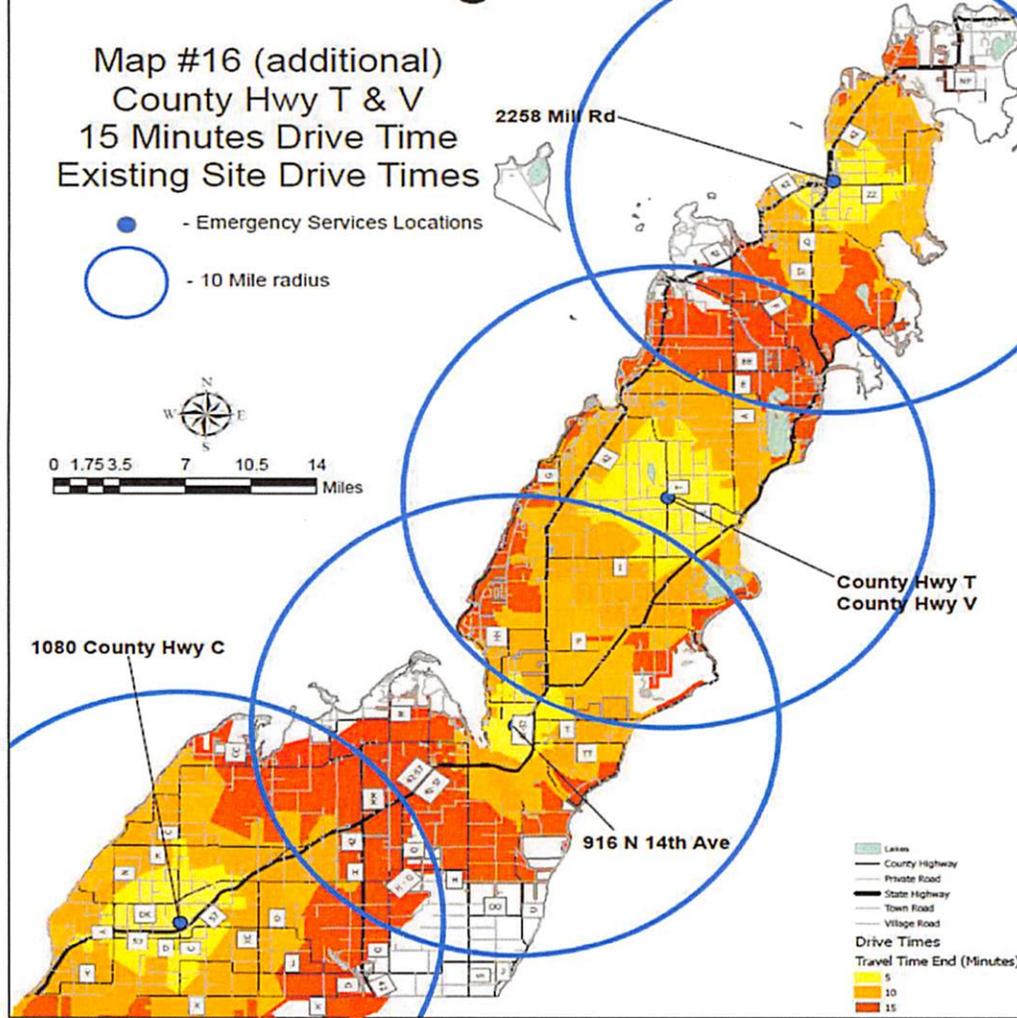


5 Minutes:
(61 / 306) * 100 = 19.93%
Photo 1

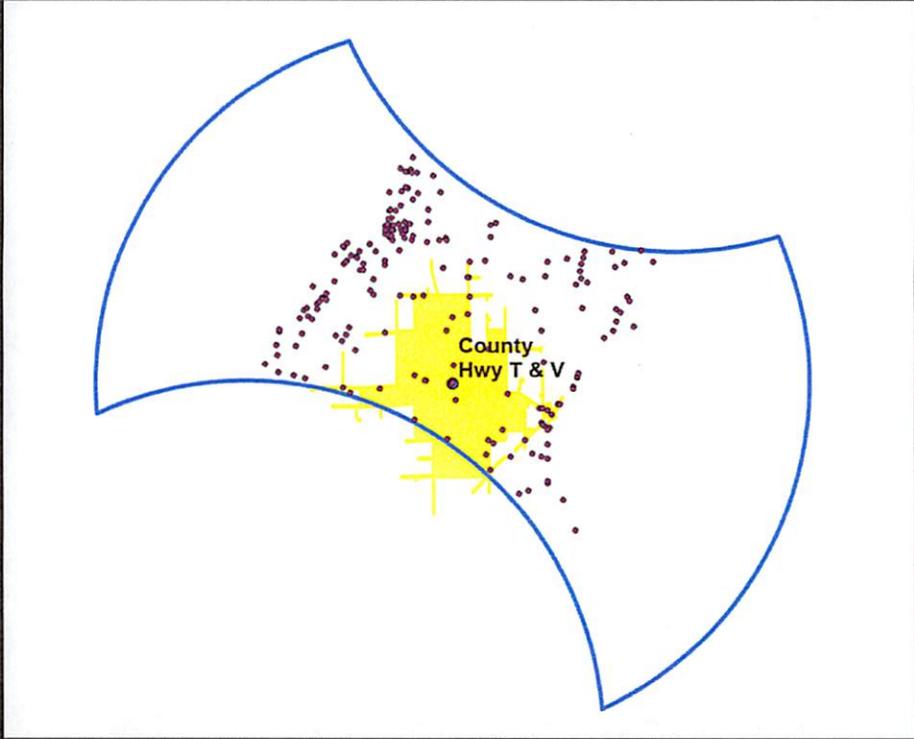

10 Minutes:
(244 / 306) * 100 = 79.73%
Photo 2

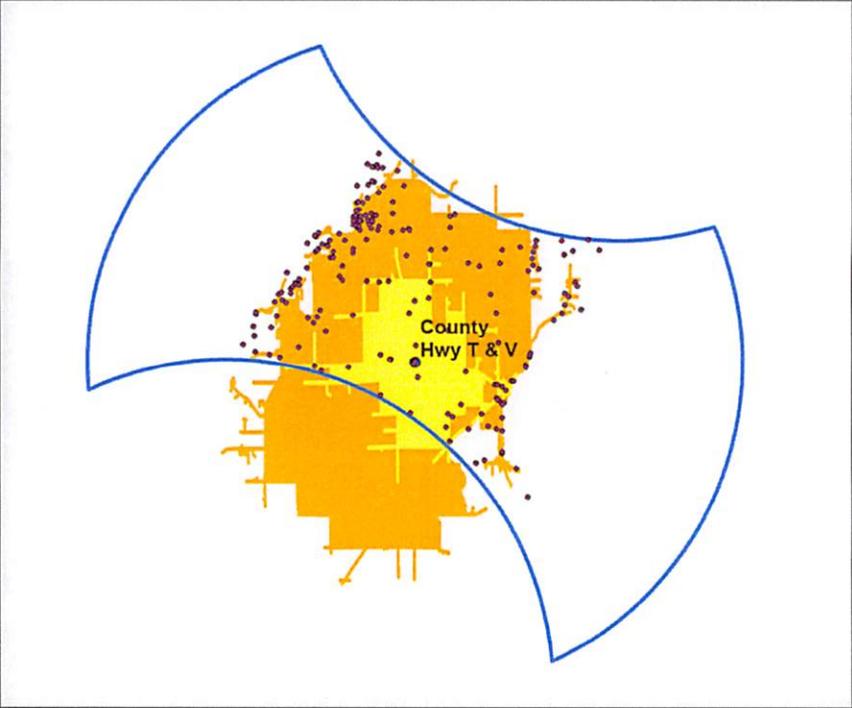

15 Minutes:
(297 / 306) * 100 = 97.05%
Photo 3

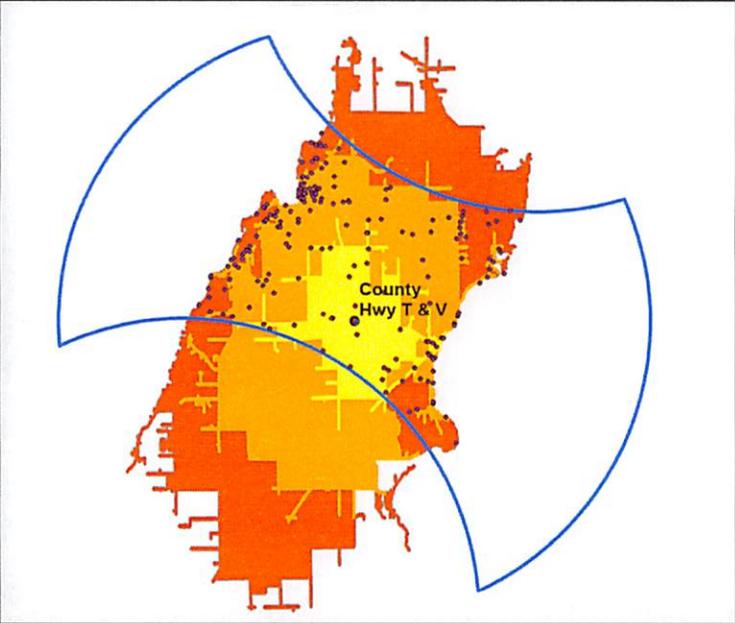


Map #8 - Village Fire Station 2023 Call Data Overlay Proposed Site Drive Times

● - Emergency Services Locations

○ - 10 Mile radius




0 1.75 3.5 7 10.5 14 Miles

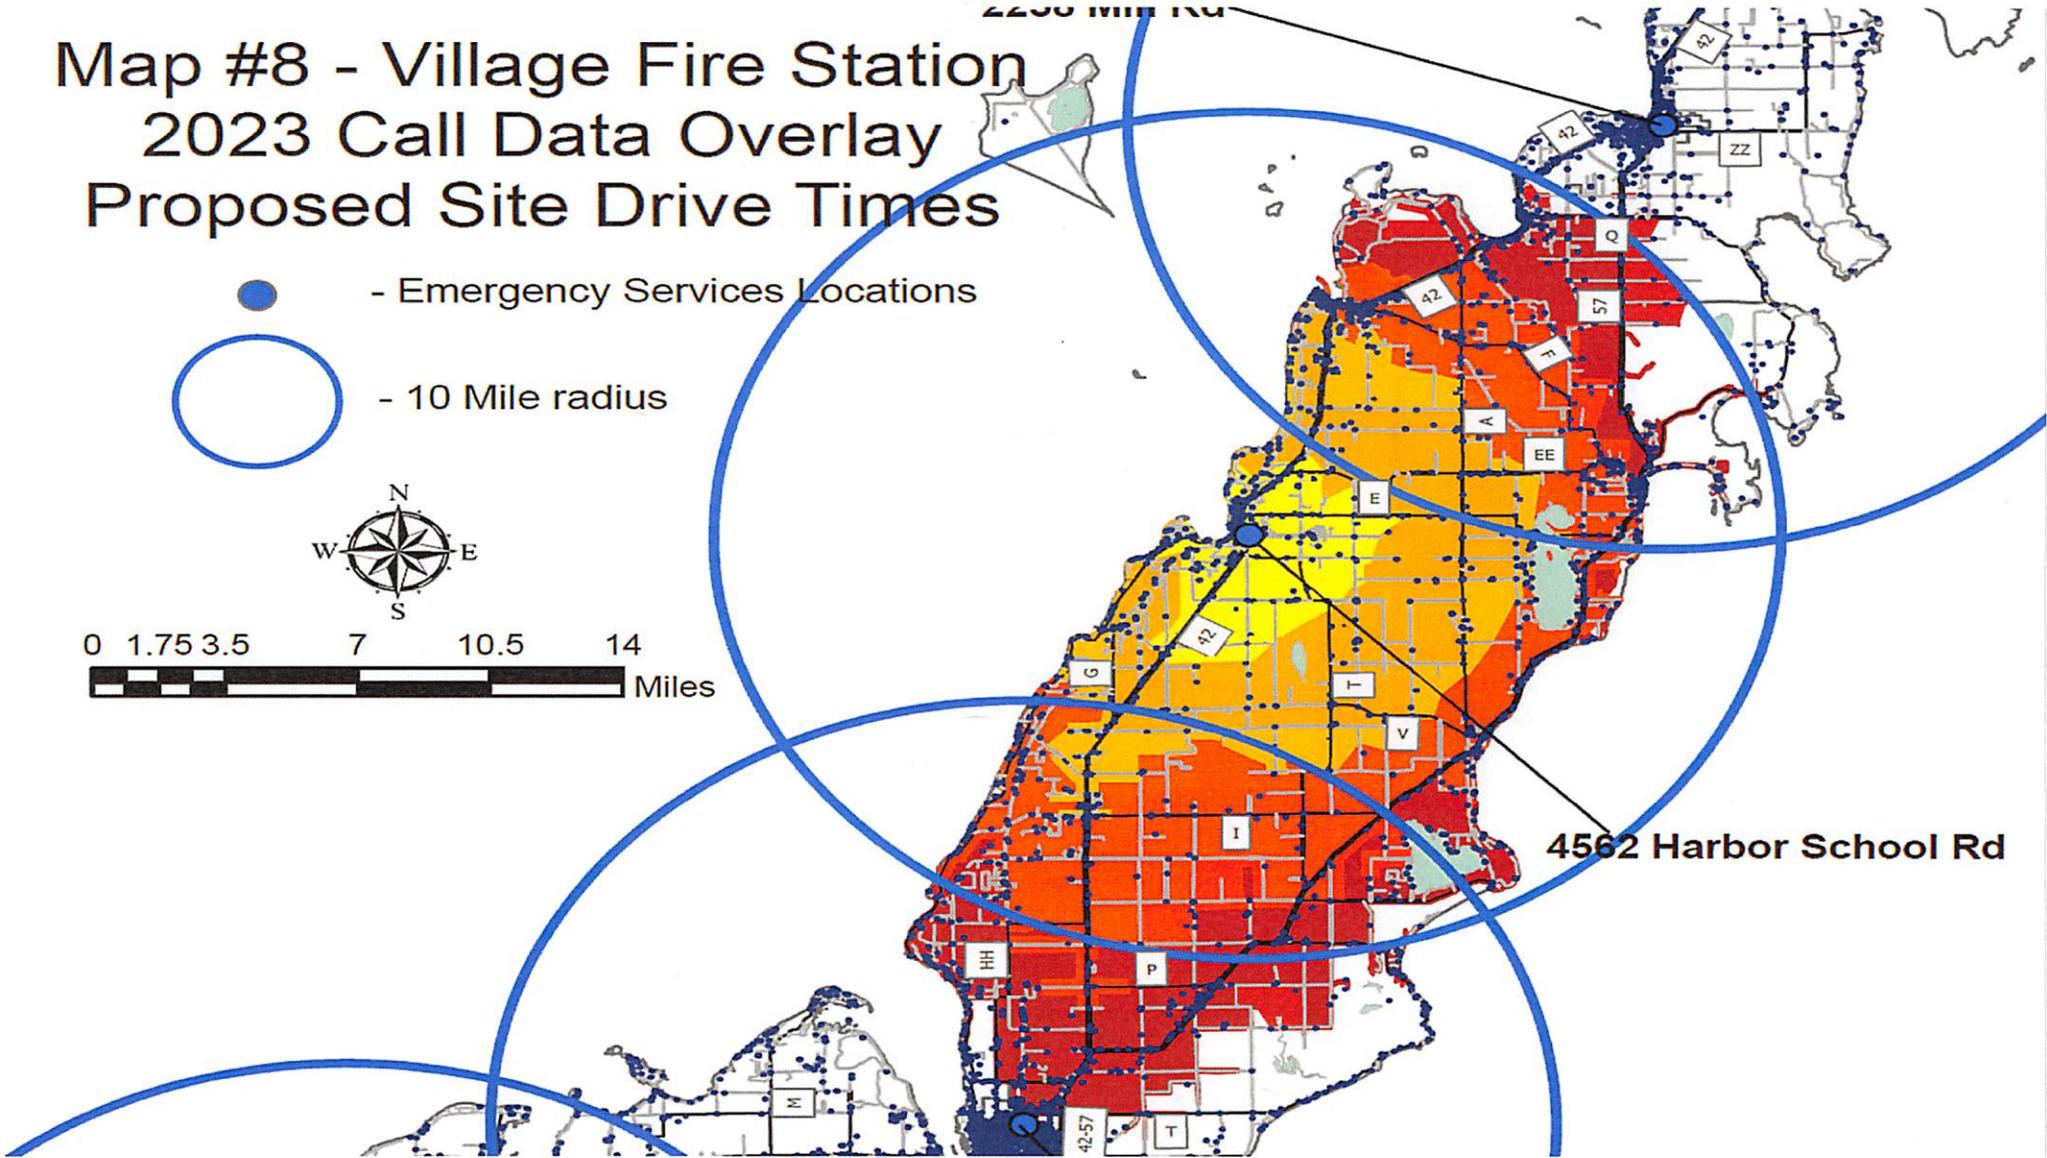

Map #7 - Jacksonport Fire 2023 Call Data Overlay Proposed Site Drive Times

● - Emergency Services Locations

○ - 10 Mile radius

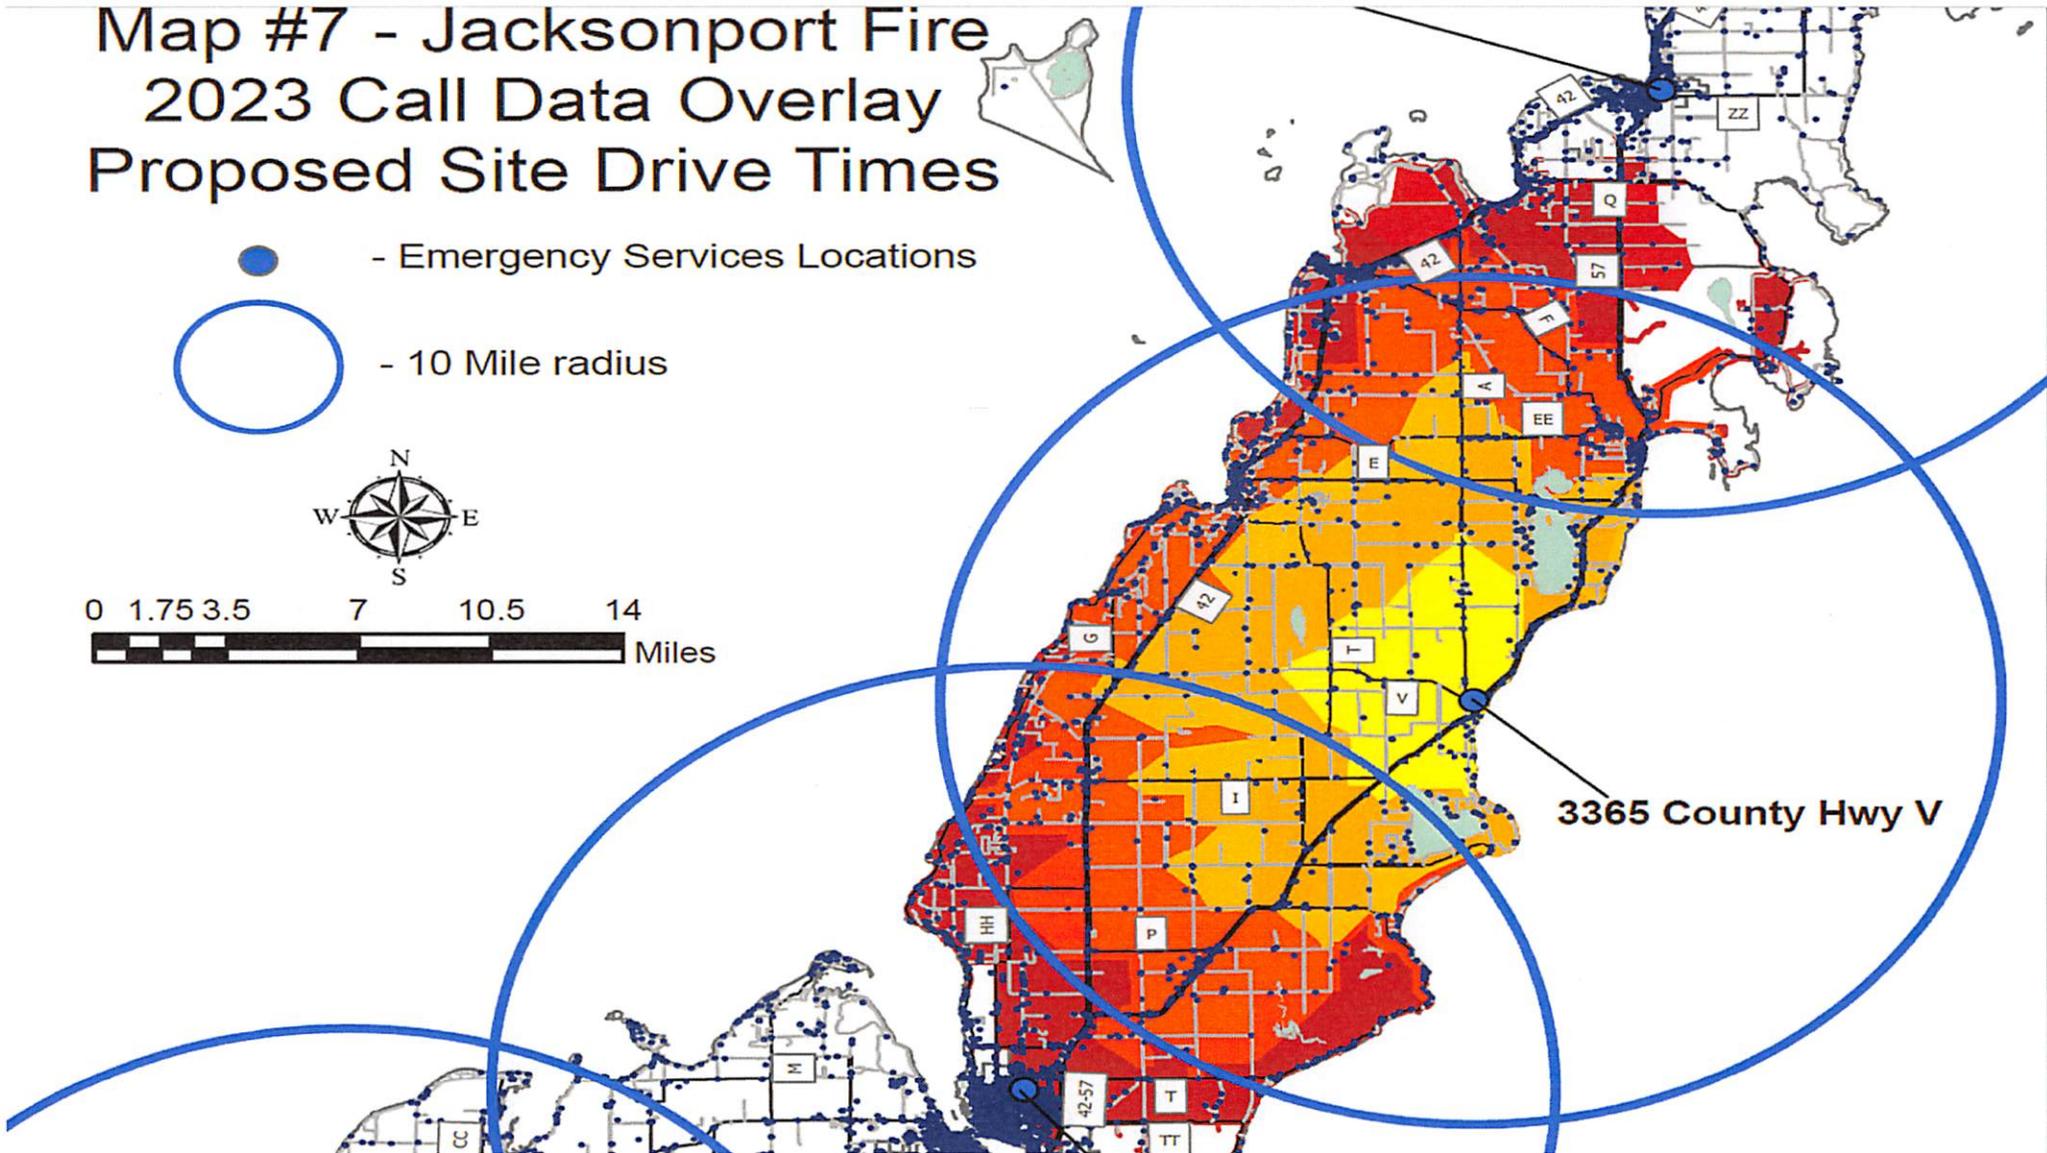


3365 County Hwy V

2023 Call Data Overlay Proposed Site Drive Times

● - Emergency Services Locations

○ - 10 Mile radius

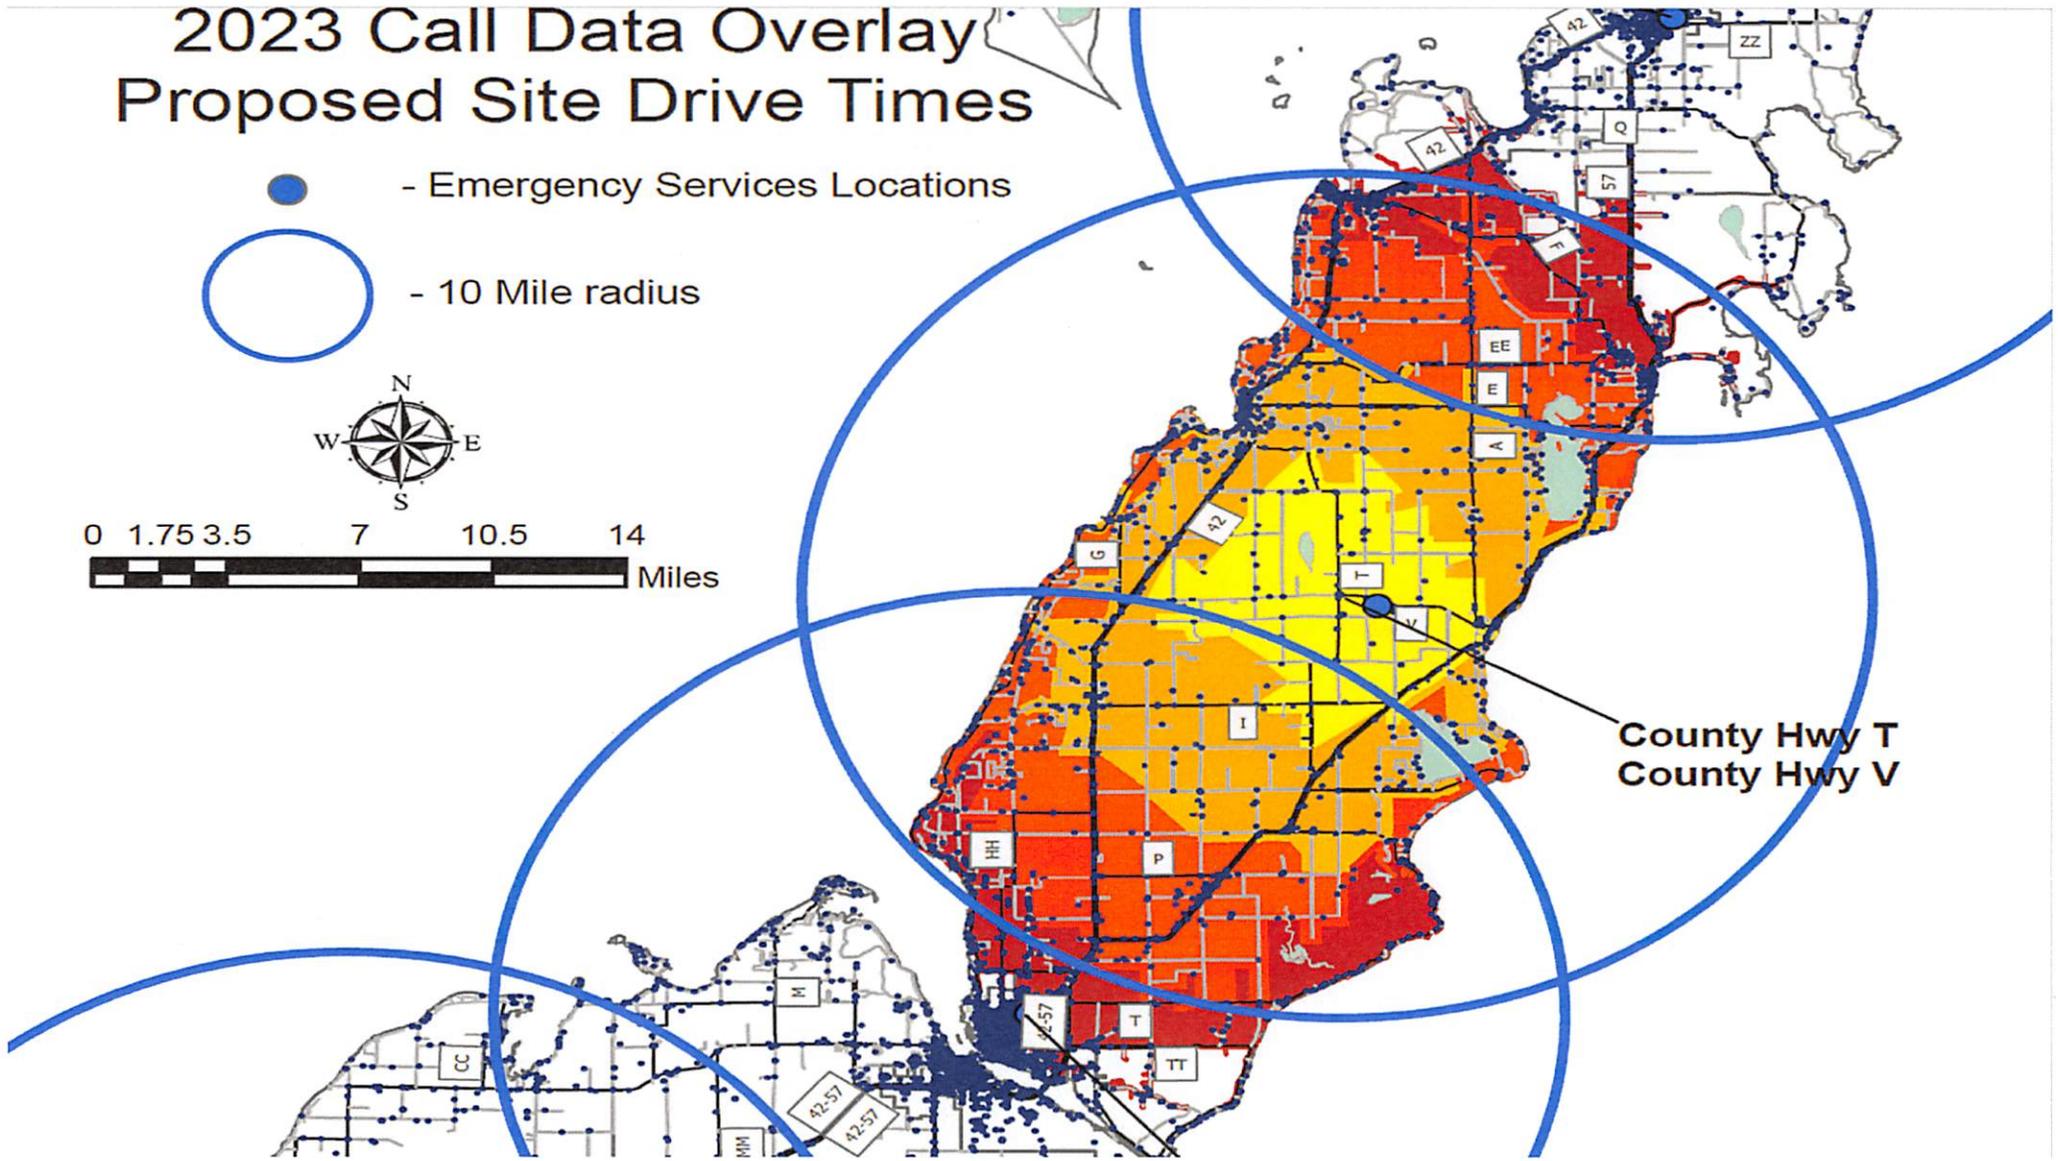

County Hwy T
County Hwy V

Project Details	
Project Name	Door County Public Safety Radio System Upgrade
Reporting Period	12/9/2025-03/10/2026
Report Date	3/10/25
Project Manager	Ashley DeGrave
Total Project Completion	9.15%

Phase 1 Project Details							
Objective	Sub-Objective	Tasks	Task Lead	Status	Completion %	Anticipated Completion	Notes

Site Finalization					38%		
	Ellison Bay - ECB		Adam - ECB	In Progress	50%		
	Structural Analysis		Adam - ECB	In Progress	50%		2/19/26 - Status call with ECB - They are still working to determine any structural enhancements. Door County continuing to pursue alternative plan
	Ellison Bluff County Park / Surrounding Areas			In Progress	5%		Due to easement restrictions leading to Ellison Bluff County Park, we are exploring nearby parcels
	Property Selection/Purchase		Edge Consulting/Nsight	In Progress	25%		10/21 - Site walk completed with Edge
	Site Survey		Edge Consulting/Nsight	Not Started	0%		
	FCC/FAA Filings		Edge Consulting/Nsight	Not Started	0%		
	Zoning/Permitting		Edge Consulting/Nsight	Not Started	0%		
	Site Studies (Enviro/Historical/Tribal)			Not Started	0%		
	Escavating			In Progress	5%		Property discussions on hold - Awaiting Ephraim/Ellison Bluff Placements before property negotiations
	Property Selection/Purchase		Edge Consulting/Nsight	In Progress	25%		Nsight did property drive-thrus and identified two interested parties on HWY ZZ Waiting to make additional contact until Ellison Bluff/Ephraim are determined
	Site Survey		Edge Consulting/Nsight	Not Started	0%		
	FCC/FAA Filings		Edge Consulting/Nsight	Not Started	0%		
	Zoning/Permitting		Edge Consulting/Nsight	Not Started	0%		
	Site Studies (Enviro/Historical/Tribal)			Not Started	0%		
	Town of Ephraim			In Progress	5%		2/10/26 - Attended Village Board Meeting w/ sample tower placements Village requested site be moved to back of parcel Edge updating maps for Village approval, then will start with site testing
	Property Selection/Purchase		Edge Consulting/Nsight	In Progress	25%		12/15 - Site Walk Completed, three possible locations identified. Edge to prepare plans to be presented to town for final selection
	Site Survey		Edge Consulting/Nsight	Not Started	0%		
	FCC/FAA Filings		Edge Consulting/Nsight	Not Started	0%		
	Zoning/Permitting		Edge Consulting/Nsight	Not Started	0%		
	Site Studies (Enviro/Historical/Tribal)			Not Started	0%		
	Highway North Shop		Edge Consulting/Nsight	On-Hold	40%		Awaiting determination on ECB site to finalize Discussion to be had with Village on Tower Restrictions, possible relocation to nearby parcel in Town of Libery Grove
	Property Selection/Purchase		Edge Consulting/Nsight	Completed	100%		County Owned Property
	Site Survey		Edge Consulting/Nsight	Completed	100%		Site Survey Completed/Received Back
	FCC/FAA Filings		Edge Consulting/Nsight	On-Hold	0%		
	Zoning/Permitting		Edge Consulting/Nsight	On-Hold	0%		
	Site Studies (Enviro/Historical/Tribal)			Not Started	0%		
	Baileys Harbor		Edge Consutling/Nsight	In Progress	40%		2/24/26 - Purchase documents completed and signed Edge to start parcel review to complete offer contingency reviews
	Property Selection/Purchase		Edge Consulting/Nsight	Completed	100%		Offer documents completed - 2/24/26

	Site Survey	Completed	100%	Site Survey Completed 4/7 and returned 4/23
	FCC/FAA Filings	In Progress	0%	Edge starting process to complete
	Zoning/Permitting	In Progress	0%	Edge starting process to complete
	Site Studies (Enviro/Historical/Tribal)	In Progress	0%	Edge to start completing as weather permits
Claybanks	Edge Consulting/Nsight	In Progress	2%	1/20/26 - Recieved communication from DNR regarding possible expemptpoin vs parcel conversion in the matter of public safety 2/16/26 - Attended Town Meeting to discuss previously restricted DNR Parcel Town would like to see upper LaSalle parcel explored prior to town parcel 2/24/26 - OCG ran coverage, came back acceptable, however after site walk w/Edge - due to such a thin parcel development would be difficult Exploring possible neighboring parcels
	Property Selection/Purchase	In Progress	10%	2/16/26 - Town not interested in persuing S Lake Michigan Dr Parcel at this time and requested further investigation of Upper LaSalle parcel
	Site Survey	Not Started	0%	
	FCC/FAA Filings	Not Started	0%	
	Zoning/Permitting	Not Started	0%	
	Site Studies (Enviro/Historical/Tribal)	Not Started	0%	
Big Hill Tower	City of Sturgeon Bay	Completed	100%	Currently Complete - EMS Central Tower is a viable location
EMS Central Tower	Sturgeon Bay	Completed	100%	9/11 - Working with Edge on bid documents and project management plan 1/20/26 - Received communication from the DNR they believe an exemption could be applied for vs a parcel conversaion in the name of Public Safety Gathering all necessary documents to submit
Murphy Park - Horseshoe Bay	Edge Consulting/Nsight	In Progress	20%	
	Property Selection/Purchase	Completed	100%	
	Site Survey	Not Started	0%	
	FCC/FAA Filings	Not Started	0%	
	Zoning/Permitting	Not Started	0%	
	Site Studies (Enviro/Historical/Tribal)	Not Started	0%	
Bayshore Drive	Edge Consulting/Nsight	On-Hold	0%	Awaiting Horseshoe Bay site selection to determine search radius
	Property Selection/Purchase	On-Hold	0%	
	Site Survey	Not Started	0%	
	FCC/FAA Filings	Not Started	0%	
	Zoning/Permitting	Not Started	0%	
	Site Studies (Enviro/Historical/Tribal)	Not Started	0%	
Sevastopol	Edge Consulting/Nsight	In Progress	42%	12/10/25 - Purchase documents completed Working with Edge for all necessary studies/reviews to check off all contingencies
	Property Selection/Purchase	Completed	100%	Will present survey and have further purchase discussions
	Site Survey	Completed	100%	Survey Competed 4/8 & returned 4/18.
	FCC/FAA Filings	In Progress	0%	Edge starting process to complete
	Zoning/Permitting	In Progress	0%	Edge starting process to complete
	Site Studies (Enviro/Historical/Tribal)	In Progress	10%	11/25 - Edge was able to comple archeological study

Phase 2 Project Details							
Objective	Sub-Objective	Tasks	Task Lead	Status	Completion %	Anticipated Completion	Notes
New Site Construction				Not Started	0%		
Existing Site Readiness				Not Started	2%		
	Existing Door County Sites			Not Started	6%		
	EMS Central		Ashley DeGrave	On-Hold	30%		2/10/26 - Edge drafted preliminary drawings & started bid documents Waiting for vendor selection to verify equipment/space required before going out for bid
		Tower Design/Drawings		Completed	100%		8/14 - Tower designed received and approved with heights of 132ft
		Bid Document Preparation		On-Hold	50%		On-Hold for vendor selection
		Construction Bid Receive/Accept Construction		Not Started	0%		
		Inspection		Not Started	0%		
	Mill Road			Not Started	0%		
	Andreas Pit			Not Started	0%		
	Sunnyslope			Not Started	0%		
	Justice Center			Not Started	0%		
	Existing Cellcom Sites			Not Started	0%		
	Other Existing Sites			Not Started	0%		
Radio Vendor Selection				In Progress	33%		
	ITN Document Preparation			Completed	100%		1/14/26 - First draft of documents received from OCG
	ITN Release - DemandStar			Completed	100%		Documents reviewed thru Jan/Feb with final draft completed last week Bid Released 2/27/26 @ 9am
	Pre-Proposal Meeting/Site Walks			In Progress	0%		Mandatory Site Walks will be March 23rd-26th - OCG On-Site
	Proposal Due Date			Not Started	0%		May 11th, 2026 - 3pm
	Proposal Opening / Review Committee			Not Started	0%		May 12th - 29th, 2026
	Committee Proposal Acceptance/Award			Not Started	0%		
	Public Safety			Not Started	0%		
	County Board			Not Started	0%		

Phase 3 Project Details							
Objective	Sub-Objective	Tasks	Task Lead	Status	Completion %	Anticipated Completion	Notes
Stakeholder Finalization				Not Started	0%		
Equipment Purchase				Not Started	0%		
Equipment Installations				Not Started	0%		
Frequency Coordination				Not Started	0%		4/28/25 CATS Meeting - Will hold off on frequency coordination and continue to evaluate at CATS for best time to move forward
User Training				Not Started	0%		
System Testing				Not Started	0%		
System Implementation/Go-Live				Not Started	0%		
Old System Decommission/Equipment Removals				Not Started	0%		
Grant Applications				In Progress	46%		
	2024 DOJ Grant Appropriation		Ashley DeGrave	In Progress	83%		New Award Period End - 3/31/27
	Application			Completed	100%		
	Acceptance / Denial			Completed	100%		
	Award Period			In Progress	50%		Grant Award Extension Applied for and approved 2/20/26
	2026 DOJ Grant Appropriation			Completed	100%		
	PSAP			Not Started			
	Innovation Grant			Not Started			



December 18, 2025

Door County Sheriff's Office
Attn: Sheriff Tammy Sternard
1201 S. Duluth Ave
Sturgeon Bay, WI 54235

RE: 2025 ALERT Grant Program Award

Dear Sheriff Sternard:

On behalf of the Wisconsin County Mutual Insurance Corporation Board of Directors and Loss Prevention-Workers' Compensation Advisory Committee, let me extend my thanks for your agency's 2025 ALERT Grant Program submission. We are pleased to inform you that your 2025 ALERT Grant Program request has been approved in the amount of \$2,000 in support of an FPV Drone.

Congratulations!

We thank you for your continued support of the Wisconsin County Mutual Insurance Corporation.

Happy Holidays,

A handwritten signature in black ink, appearing to read "Josh Dirkse". The signature is fluid and cursive, written over a white background.

Josh Dirkse
Senior Vice President – Client Services

Wisconsin County Mutual Insurance Corporation

Corporate Management • Wisconsin Counties Association
22 East Mifflin Street, Suite 900, Madison, WI 53703 ◀ p 866.404.2700 • 608.663.7188 • f 608.663.7189 ◀ www.wisconsincountymutual.org

General Administrator • Aegis LLC: A Charles Taylor Company
18550 West Capitol Drive, Brookfield, WI 53045-1925 ◀ p 800.236.6885 • f 262.781.7743 ◀ www.aegis-corporation.com

March 3, 2026

Door County Technology Services
Government Center
421 Nebraska Street
Sturgeon Bay, WI 54235

Dear Door County,

Thank you for the opportunity to provide you with this proposal for a robust and comprehensive service plan. This plan will keep the software that runs the other critical systems at the Jail up to date. Furthermore, included with this service plan you will have many other benefits that include priority service, discounted labor and material rates, reduced vehicle charges and more.

SCOPE OF WORK

SGTS, Inc. will provide ongoing software maintenance and service as required.

INCLUDES

SGTS, Inc. shall be responsible for the above listed scope of work, and the following items:

- Annual Software Updates and Upgrades²
 - WonderWare version updates
 - Windows patches and security updates
 - Camera Callup Updates as Required and Management of Camera Callups
- SGTS, Inc. Premium Level Service Plan

Service	Service Plan Offerings			
	No Plan	BASIC	PREMIUM	ENTERPRISE
Remote Response	3 Business Days	One Business Day	Same Day	W/in 2 hours
On-Site Response	Scheduled	< 1 week	1 - 4 bus days	1 business day
Included Support Hours	-	-	Up to 10/mo	Up to 25/mo
Includes Annual ER hours	-	-	8/yr.	16/yr.
Additional Hours Discount	-	10% off	15% off	20% off
Parts Warranty	0 days	90 days	6 months	Lifetime
Life Cycle Planning	\$1,995	\$995	\$495	Included
Account Reviews	-	Annually	Quarterly	As requested
Prioritization Fee	\$250	\$150	No Charge	No Charge
Vehicle Surcharge	\$799	\$599	\$399	\$199
TTM to remove vehicle surcharge	NA	\$175,000	\$125,000	\$100,000
Per Diem (Overnight Only)	\$250	\$125	No Charge	No Charge

EXCLUDES

SGTS, Inc. shall not be responsible for anything not listed in the above scope of work, and the following items

- Any and all liability for data breaches, hacks of any kind at any time
- Future integration or resolution of errors that occur as a result of Verkada system and/or software changes, upgrades, or updates, or other factors, including services or components additions, removals, or changes by others outside our control that would render the deployed integration unusable or insufficient.

REQUIREMENTS

SGTS, Inc. will need the following items prior to implementation

- Executed Professional Services Agreement

- Remote Access to the Jail Control System and Network
- Remote access at **Full Administrator** permission to the live/final Verkada Command system/platform

INVESTMENT

- Monthly (standard - \$1,593/mo.)
 - **3 Year Term** **\$19,120/year**
- **Contract Total** **\$57,362.00**

TERMS

(Note Pricing & Terms subject to change after 30 days)

- Net 30 Terms
- Invoiced Annually - April 1, 2026/2027/2028

We look forward to working with you.

Chloe James

Strategic Account Manager



Door County Emergency Services

916 N 14th Ave.
Sturgeon Bay, WI 54235


Aaron LeClair, Director

03/04/2026

TO: Public Safety Committee



FROM: Aaron LeClair

RE: Operations Summary – February 2026

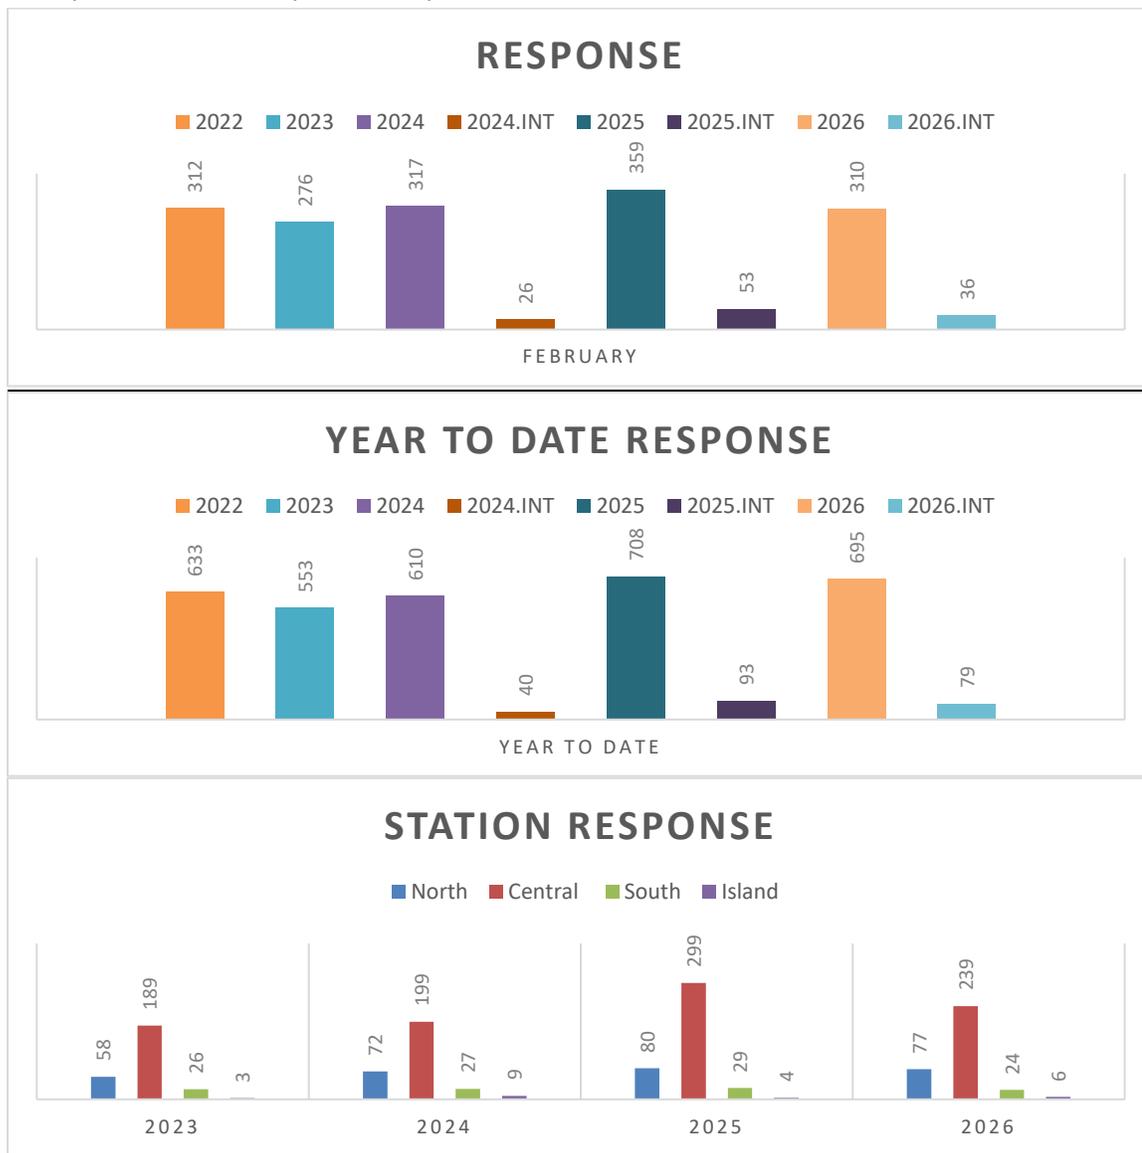

Response:

	Primary	2 nd	3 rd	4 th
February	266	71	9	0

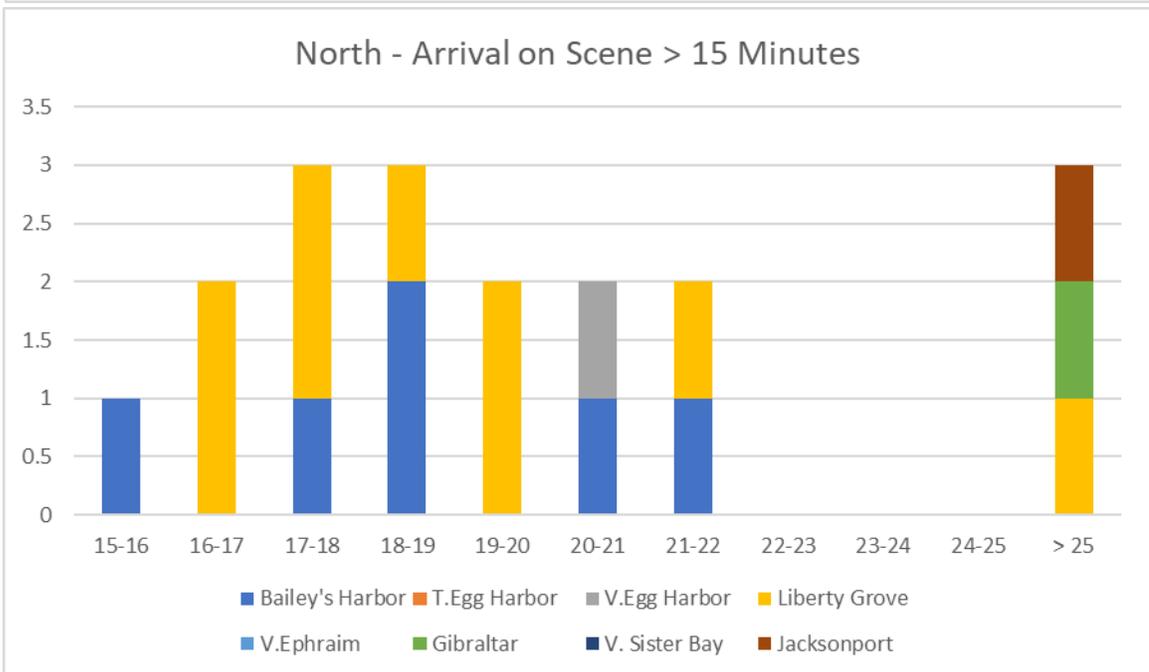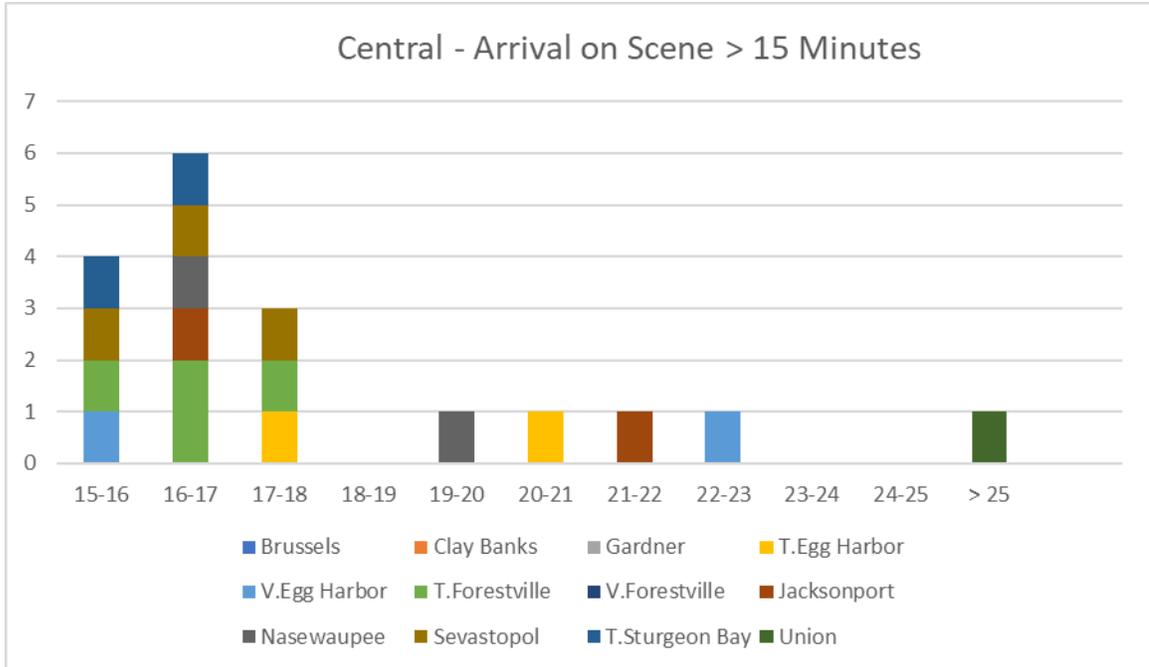




Door County Emergency Services

916 N 14th Ave.
Sturgeon Bay, WI 54235

Aaron LeClair, Director

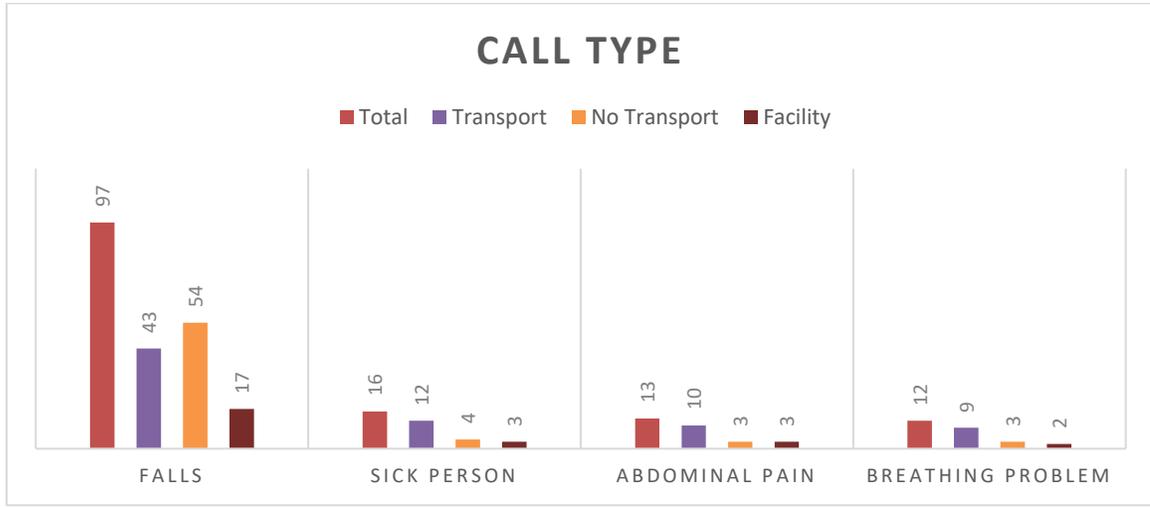

DCMC Transfers:

- Provided 36 transfers: ALS 29 BLS 7

Fall Prevention:

- Providing follow up phone calls and home visits to patients referred by crews.

Training - Recruitment:

- Personnel are participating on-line, in-house training programs, and Squad Meetings.
- Two EMTs continue in paramedic school.
- Two EMTs completed orientation and start field training March 6th.

Staffing:

<u>Full-time Paramedic:</u>	24 of 24 positions filled.
<u>Casual Call Paramedic:</u>	10 of 10 positions filled.
<u>Full-time EMT/AEMT:</u>	6 of 6 positions filled.
<u>Casual Call EMT/AEMT:</u>	25 of 25 positions filled.
<u>On Call EMT/AEMT (Island):</u>	15 of 20 positions filled.
<u>Captain:</u>	2 of 3 positions filled.
<u>Billing Specialist:</u>	2 of 3 positions filled.

Emergency Management:
Verbal update

**Door County
Request for Year End Carry Overs
Year Ending: 2025**

Department Name: _____ Emergency Services

The following carry over accounts were approved by the Judiciary/Public Safety Committee at their meeting on 03/10/2026

Account Name	Account Number:		Sub-Dept Cost Center	Account #	Detail	Amount
	Fund	Dept #				
Capitol	100	29	2112	69901		36520

Total Carry Over Amount

36,520.00

Reason for Carry Over: Funds were budgeted for the replacement of carpeting and epoxy floor repair at the north station.
The project needs to be coordinated with Sister Bay/Liberty Grove Fire. We anticipate the
project happening in 2026.

Preparer's Signature: _____


Dept Head's Signature: _____


Date: 2/26/2026

Funds Verified by Finance Director: _____

Date Verified: _____



DOOR COUNTY

Resolution No. 2026-___

APPROVAL OF COMMUNITY INVESTMENT FUND GRANT TO EMERGENCY MANAGEMENT FOR SAFETY BARRIERS

TO THE DOOR COUNTY BOARD OF SUPERVISORS:

ROLL CALL Board Members	Aye	Nay	Exc.
Dist. 1 D. Englebert			
Dist. 2 T. Thayse			
Dist. 3 <i>vacant</i>			
Dist. 4 N. Robillard			
Dist. 5 J. Miller			
Dist. 6 K. Fisher			
Dist. 7 C. Morkin			
Dist. 8 C. Jeanquart			
Dist. 9 R. Shaw			
Dist. 10 P. Rockwell			
Dist. 11 M. Rusnak			
Dist. 12 N. Norton			
Dist. 13 D. Vogel			
Dist. 14 H. Zettel			
Dist. 15 E. Gauger			
Dist. 16 D. Enigl			
Dist. 17 B. Bultman			
Dist. 18 V. Hancock			
Dist. 19 <i>vacant</i>			
Dist. 20 W. Kalms			
Dist. 21 J. Gunnlaugsson			

BOARD ACTION

Vote Required: Majority Vote of a Quorum

Motion to Approve Adopted

1st _____ Defeated

2nd _____

Yes: _____ No: _____ Exc: _____

Reviewed by: _____, Corp. Counsel

Reviewed by: _____, Administrator

FISCAL IMPACT: The donated funds will be used for the specified purpose; no additional County funds are required because of the acceptance of this donation. STW

Certification:

I, Jill M. Lau, Clerk of Door County, hereby certify that the above is a true and correct copy of a resolution that was adopted on the 24th day of March, 2026 by the Door County Board of Supervisors.

 Jill M. Lau
 County Clerk, Door County

1 **WHEREAS**, Sec. 59.52(19) Wis. Stats. empowers a county board to accept
 2 donations, gifts, or grants of money for any public governmental purpose within the
 3 powers of the county; and

4
 5 **WHEREAS**, Resolution 75-84 entitled “Gifts, Grants & Donations to the
 6 County of Door” requires approval of the Door County Board of Supervisors, for
 7 acceptance of all donations, gifts, and grants whether in the form of money, or
 8 personal or real property; and

9
 10 **WHEREAS**, Pursuant to Rule of Order No. 39, the County Board is to be
 11 provided notice of and must approve any donation, gift or grant equal to or in
 12 excess of \$5,000.00 prior to acceptance; and

13
 14 **WHEREAS**, The Door County Emergency Management Department
 15 requested funds to assist with the purchase of safety barriers to enhance the
 16 public’s safety at outdoor events throughout Door County; and

17
 18 **WHEREAS**, The Door County Community Foundation, Inc, via the Community
 19 Investment Fund Grant, has approved a grant award to the County of Door in the
 20 amount of \$100,000 for the purchase of safety barriers. This grant supports the
 21 County of Door’s efforts to improve the safety of the community at outdoor events;
 22 and

23
 24 **WHEREAS**, The Public Safety Committee has voted to support accepting the
 25 above-described grant in the amount of \$100,000.

26
 27 **NOW THEREFORE, BE IT RESOLVED**, That the Door County Board of
 28 Supervisors does hereby authorize the Door County Emergency Management
 29 Department to accept the grant as described above.

30
 31 **SUBMITTED BY: JUDICIARY & PUBLIC SAFETY COMMITTEE**

_____	_____
Joel Gunnlaugsson, Chair	Philip Rockwell
_____	_____
Nancy Robillard	Dale Vogel
_____	_____
Collin Jeanquart	

Ryan Shaw	



PITAGONE F18 MOBILE VEHICLE BARRIER

The Pitagone F18 is a modular, rapidly deployable vehicle barrier for any special event.



The Pitagone F18 Mobile Vehicle Barriers are a lightweight, unique and mobile solution designed to protect people, places and things against intentional or inadvertent vehicle ramming attacks.

These mobile barriers can be set up in a matter of minutes by one person and does not require any tools to configure them. They are the only crash certified mobile solution crash tested with the wheels on the barrier. The integrated wheels on each barrier allows for emergency vehicle access. Pitagone F18 is a modular system, meaning the barriers can connect to each other to provide unlimited protected coverage. Optional Barrier Trailer Kits are available.



Pitagone Barrier Details

- **Crash Certifications:**
 - ASTM: F2656/F2656M-20 PU30/P3
 - PAS 68: 2013
 - IWA 14-1: 2013
 - German Certification:**
 - 45 degree Impact Attack
 - 10.4 ft Offset Impact Attack
 - Wet Road Surface
- Emergency Vehicle Access Capabilities
- Available for purchase or rental
- Custom Color Schemes
- Barrier Trailer Kits
- Highly Visible
- Requires No Tools For Set Up
- No Sharp Edges
- Adjustable With Two Widths
- Secure & Stackable Storage
- Crash Tested with Wheels On
- Integrated ADA Accessible Pedestrian Walk Through

GET IN TOUCH

A leader in mobile high-security fencing, vehicle barriers, crowd control measures, guard booths, and temporary perimeter security solutions.



 VISIT SITE



ARX Perimeters
708-352-2373
arxperimeters.com
421 Heathrow Court
Burr Ridge, IL 60527



Door County Communications Center

1201 S Duluth Ave
Sturgeon Bay, WI 54235


Director: Brenda Bley
(920) 746-2407
bbley@co.door.wi.us

Communications Monthly Report February 2026

Call Volume

	February 2026	YTD 2026	February 2025	YTD 2025
911 Line	510	1,138	600	1,268
Non – Emergency	1,677	3,918	1,960	3,895
Total	2,187	5,056	2,560	5,163

Peak Call Times

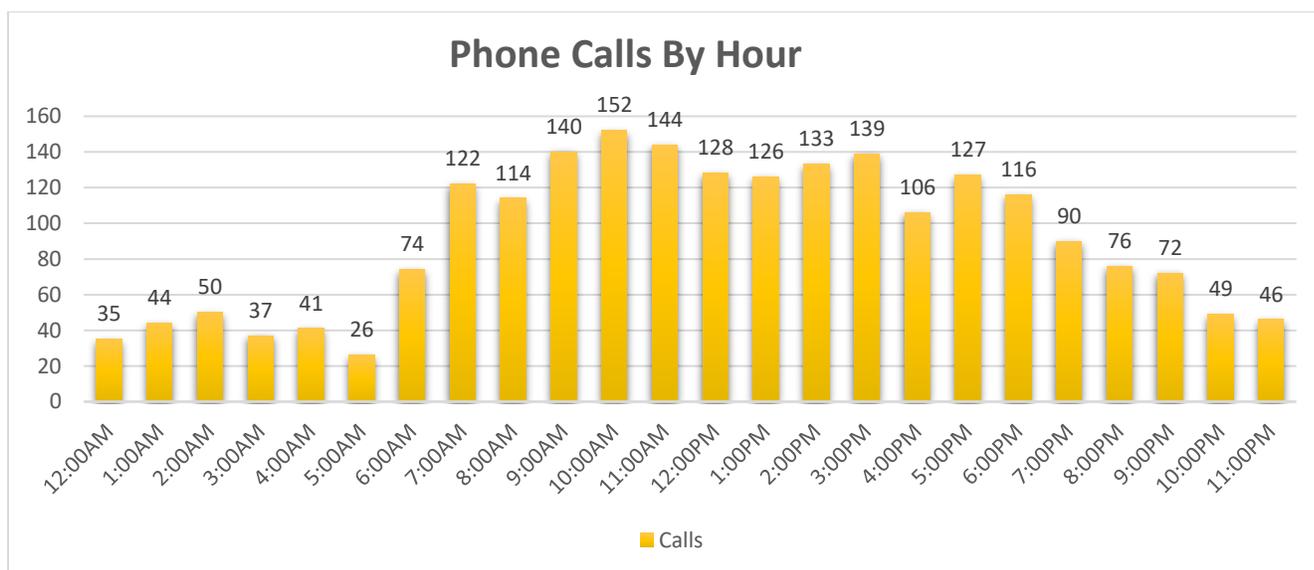

Top 5 Calls

1. 911 Follow Up – 5.06%
2. Citizen Assist – 4.32%
3. Fall – 3.18%
4. Medical Emergency – 3.13%
5. Car in the Ditch – 2.16%

Staffing

- 11 Total staff
- 10 Full Time – including 2 Leads
- 1 Training
- 0 Onboarding
- 1 Open Position

Door County
Request for Year End Carry Overs
Year Ending: 2025

Department Name: Door County Communications Center

The following carry over accounts were approved by the
 Committee at their meeting on (mm/dd/yyyy)

Account Name	Account Number:		Sub-Dept Cost Center	Account #	Detail	Amount
	Fund	Dept #				
Conference Fees & Training	100	69	1158	54101		7,652.94
Operational Expenses	100	69	1158	59153.005		3,726.77
SC-Software Dispatch	100	69	1158	52302.00069		3,356.43

Total Carry Over Amount

14,736.14

Reason for Carry Over:

Attend Spillman Summit

Cover the Cost of Vesta phone warranty not covered by 2026 grant

Installation of new headset jacks and new adapters at the dispatch consoles

Preparer's Signature:

Brenda Bley

Dept Head's Signature:

Brenda Bley

Date:

2/12/2026

**Funds Verified by
 Finance Director:**

Steve Wipperfurth

Date Verified:

2/12/2026
